


FACTS AND FIGURES

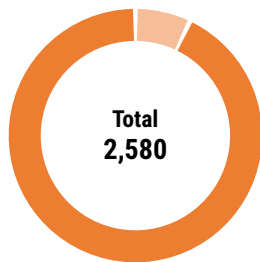

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	98.64%	39.28%
Adobe Structures	0.47%	34.86%
Reinforced Cement Concrete (RCC) Frame	0.39%	2.15%
Brick and Cement Mortar Masonry	0.23%	4.51%
Others	0.28%	19.21%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	2,154
PA Agreement	2,065 (89%)
I st Tranche received	2,060 (94%)
II nd Tranche received	1,774 (380)
III rd Tranche received	1,348 (806)

Houses

Under Construction: - Completed: -

Retrofitting Status

Total Eligible HHs	372
PA Agreement	251 (121)
I st Tranche received	246 (126)
II nd Tranche received	372

Grievances

Registered: 927
Addressed: 514

Non-compliances

Registered: -
Addressed: -

Data Updated on: 2019-05-16 00:00:00

PO Presence

Active: CECI (Agriculture), CECI (DRM), CECI (Livelihood), CECI (Governance)

Phased Out: CECI (Agriculture), CECI (DRM), CECI (Livelihood), FCA (Education), HFN (Health), LUMANTI (Shelter), MCC (Agriculture), MCC (Shelter), MCC (Hygiene), NDBS (Education), NRCS (Agriculture), NRCS (Livelihood), NRCS (Health), NRCS (Hygiene), NYF (Education), OXFAM-GB (Shelter), PLAN (Education), RICOD (Shelter)

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	39,694	-	-
Aggregate	m ³	41,032	-	-
Sand	m ³	4,242	-	-
Timber	cu. ft.	4,908	-	-
Cement (PPC)	Sack	-	-	-
Cement (OPC)	Sack	136,308	-	-
Rebars	kgs.	430,355	-	-
Tin	bundle	5,574	-	-
Bricks	pcs.	430,901	-	-

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

-/-
-/-

OTHER SECTORS



Schools

Damaged: 27
Under Construction: 20
Construction Completed: 20



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

KEY CONTACTS

Municipal Office

Gopilal Singtan
Mayor
9851168250

Municipal Office

Kabel Ghalan
Focal Person
9843003955

Municipal Office

Mingma Tamang Lama
Deputy Mayor
9843835965

DLPIU-GMaLI

Bir Bahadur Rawal
DLPIU-Chief
9851201088

Municipal Office

Rom Bahadur Mahara
Administration Officer
9851164400

DLPIU-Building

Chandra Kaji Gurung
DLPIU-Chief
9841576783

HHs WITH LAND ISSUES

No Reported Land Issues


STATUS OF TECHNICAL STAFF

Staff	Available Nos.	Additional Req. Nos.
Engineers	6	-
Sub-Engineers	9	-
Asst. Sub-Engineers	3	1
Masons	- (7 days) 7 (50 days)	- (7 days) 90 (50 days)

Source: Municipal survey


MASON TRAINING

Trainings (# out of total required)



Source: HRRP Analysis

TA ACTIVITIES MAP

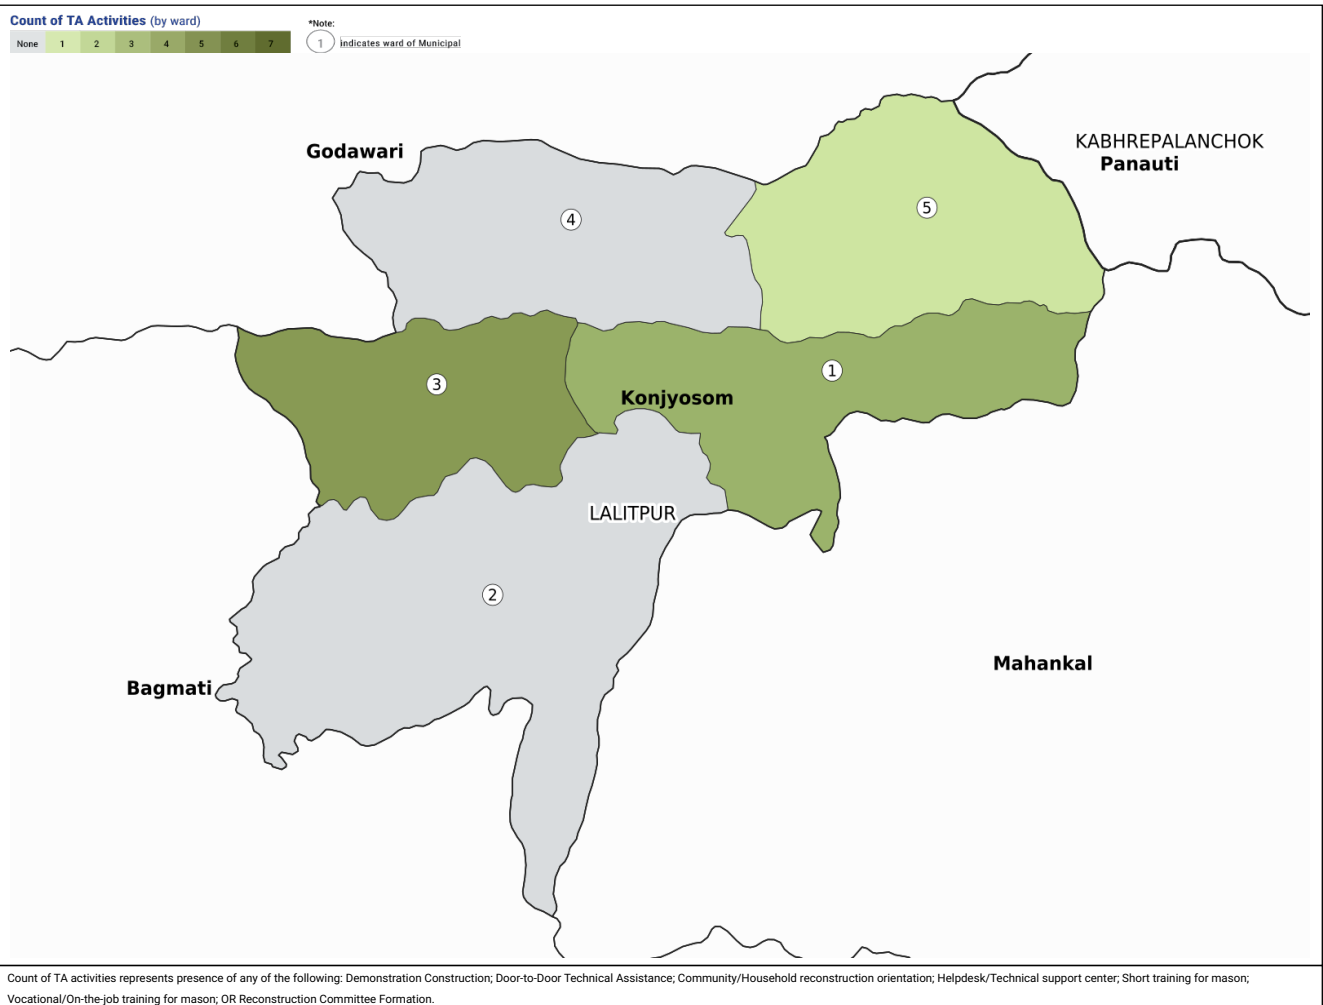

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Ambika Amatya (District Coordinator) 2. (District Technical Officer) 3. Sachin Malego (District Information Management Officer)
9841356409 9849166793
